


Harper Brothers Construction LLC		 																					
Project Title: Northpark Drive Overpass Project (T-1013)																							
Owner: Lake Houston Redevelopment Authority																							
HBC Job No: 2215																							
Date Prepared:2/01/2024																							
Prepared By: Robert Acuna																							
OPERATIONS		February							February							February/March							
		S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	
Work Location & Description	Crew	2/11	2/12	2/13	2/14	2/15	2/16	2/17	2/18	2/19	2/20	2/21	2/22	2/23	2/24	2/25	2/26	2/27	2/28	2/29	3/1	3/2	
Outfall B - 6' x 5' RCB	HBC (Juan)		X	X	X																		
12" Waterline Offset - Change Order Work	HBC (Juan)					X	X																
Set LPCB Sta 12+00 to 21+00 WB Northpark	HBC (Juan)									X													
Temporary Stripping Sta 12+00 to 21+00 WB Northpark	TS&L									X													
Outfall A - 36" RCP	HBC (Juan)										X	X	X	X			X						
Inlets and RCP Sta 13+25 to 17+50	HBC (Juan)																	X	X	X	X		
12" & 16" Waterline Testing - Chlorination	HBC (Juan)		X	X	X	X	X																
66" Cast In Place SET	HBC (Luis)		X	X	X	X	X			X	X	X											
JB 23 & 21 Walls and Top	HBC (Sostenes)		X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
Pond #1 Excavation	HBC (Rogelio)		X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
Masonry Retaining Walls (Detention Ponds)	Texas Wall and Landscape		X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		


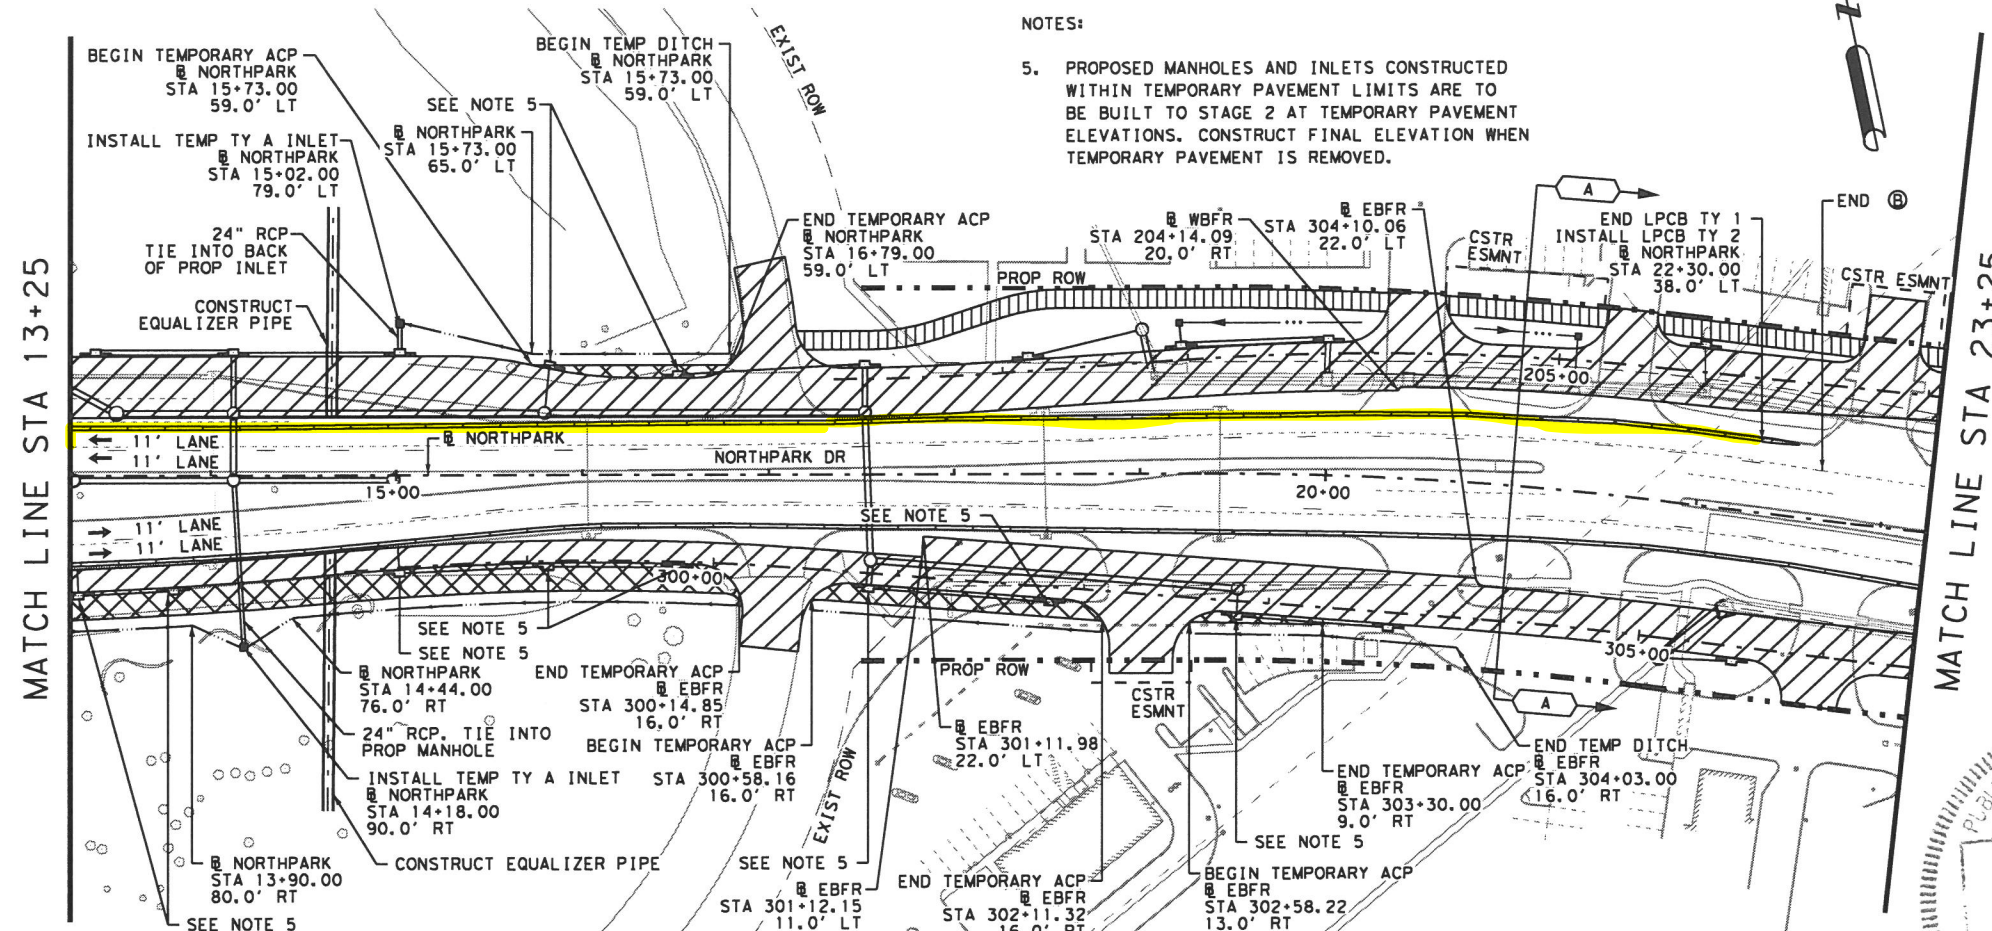


NOTES:
5. PROPOSED MANHOLES AND INLETS CONSTRUCTED WITHIN TEMPORARY PAVEMENT LIMITS ARE TO BE BUILT TO STAGE 2 AT TEMPORARY PAVEMENT ELEVATIONS. CONSTRUCT FINAL ELEVATION WHEN TEMPORARY PAVEMENT IS REMOVED.

LEGEND

	PERM CONST THIS STEP		TEMP CONST THIS STEP
	FAST-TRACK CONC CONST THIS STEP		PERM CONST PREV COMPLETED
	TEMP CONST PREV COMPLETED		SIDEPATH PREV COMPLETED
	SIDEPATH THIS STEP		PLASTIC DRUM
	TRAFFIC FLOW THIS STEP		TYPE III BARRICADE
	TEMP GROUND MOUNTED SIGN		TYPE III BARRICADE
	LOW PROFILE CONC. BARRIER (LPCB) W/ REFLECTORS @ 10' C/C		
	LPCB TY 2		
	TEMPORARY DRAINAGE		

- NOTES:
1. WHEN LOW PROFILE CONCRETE BARRIER IS ADJACENT TO TRAFFIC, ALL LOW PROFILE CONCRETE BARRIER ENDS FACING APPROACHING TRAFFIC SHALL BE PROTECTED BY LOW PROFILE CONCRETE BARRIER TY 2
 2. ACCESS TO ALL PROPERTIES AND SIDE STREETS IS TO BE MAINTAINED AT ALL TIMES. DRIVEWAY CONSTRUCTION SHALL FOLLOW HOUSTON DISTRICT CSMD TC 8010-20 AND DS TC 8020-04
 3. REFER TO "TRAFFIC CONTROL PLAN MISCELLANEOUS DETAILS" FOR TEMPORARY PAVEMENT STRUCTURE.
 4. DO NOT CONSTRUCT PROPOSED CURBS IN CONFLICT WITH TEMPORARY PAVEMENT UNTIL AFTER TEMPORARY PAVEMENT IS REMOVED.

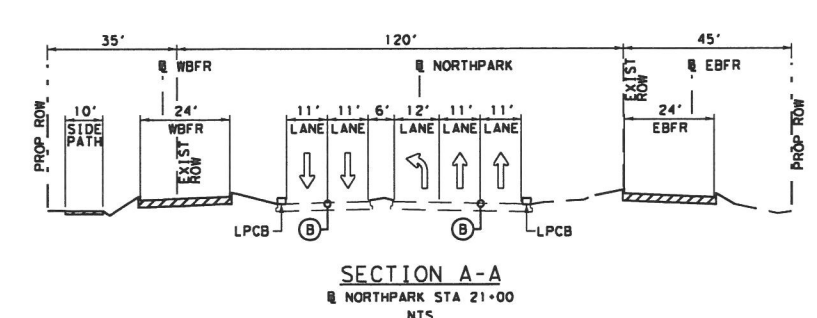

SPACING FOR CHANNELING DEVICES:

- (R) PLASTIC DRUMS ON MERGING TAPER @ 30' C-C WITH CHEVRON SIGN @ 60' C-C AND TYPE "C" WARNING LIGHT (FOR OVERNIGHT CLOSURE)
- (S) PLASTIC DRUMS ON RADII @ 5' C-C
- (T) PLASTIC DRUMS ON TANGENT @ 35' C-C WITH VERTICAL PANEL @ 70' C-C AND TYPE "C" WARNING LIGHT @ 70' C-C (FOR OVERNIGHT CLOSURE)
- (U) PLASTIC DRUMS IN FRONT OF CONSTRUCTION ZONE @ 20' C-C WITH VERTICAL PANEL @ 40' C-C AND TYPE "A" WARNING LIGHT @ 40' C-C (FOR OVERNIGHT CLOSURE)

SPACING SHOWN ON TRAFFIC CONTROL PLANS SHALL BE SUPERSEDED BY THE ABOVE SPACINGS. SPACINGS MAY BE ADJUSTED TO PROVIDE DRIVEWAYS, INTERSECTIONS, AND/OR MEDIAN OPENINGS.

- LEGEND**
- (A) WRK ZN PAV MRK REMOV (W) (4") (SLD)
 - (B) WRK ZN PAV MRK REMOV (W) (4") (BRK)
 - (C) WRK ZN PAV MRK REMOV (W) (4") (DOT)
 - (D) WRK ZN PAV MRK REMOV (W) (8") (SLD)
 - (E) WRK ZN PAV MRK REMOV (W) (12") (SLD)
 - (F) WRK ZN PAV MRK REMOV (W) (24") (SLD)
 - (G) WRK ZN PAV MRK REMOV (Y) (4") (SLD)
 - (H) WRK ZN PAV MRK REMOV (Y) (24") (SLD)
 - (I) WRK ZN PAV MRK REMOV (REFL) TY II-A-A @ 40' C/C
 - (J) WRK ZN PAV MRK REMOV (W) (ARROW)
 - (K) WRK ZN PAV MRK REMOV (W) (DBL ARROW)
 - (L) WRK ZN PAV MRK REMOV (W) (WORD)
 - (M) WRK ZN PAV MRK REMOV (W) (RR XING)
 - (N) WRK ZN PAV MRK REMOV (W) (TURN)
 - (O) WRK ZN PAV MRK REMOV (REFL) TY II-C-R @ 40' C/C
 - (Z) PREV WRK ZN PAV MRK TO REMAIN

NO.	REVISIONS	BY	DATE

HNTB
HNTB Corporation
The HNTB Companies
Infrastructure Solutions
Firm Registration Number 420

LH RA
LAKE HOUSTON REDEVELOPMENT AUTHORITY & TRIZ 10
660 HUNTON ANDREWS KURTH LLP
660 TRAVIS, SUITE 4200
HOUSTON, TX 77002

CITY OF HOUSTON
HOUSTON PUBLIC WORKS

NORTH PARK DRIVE

TRAFFIC CONTROL PLANS
PHASE 2 STEP 3
NORTH PARK DR
STA 13+25 TO STA 23+25

CSJ: 0271-03-060 SHEET 2 OF 5

DESIGNED TO	FED. RD. DIST. NO.	STATE	CITY OF HOUSTON	HIGHWAY NO.
CHECKED TO	6	TEXAS	SEE TITLE SHEET	CS
DRAWN TO	STATE DISTRICT	COUNTY	CONTROL NO.	SECTION NO.
CHECKED TO	PI	HOU	0912	37

1/7/2022 7:43:43 PM
