STEERING COMMITTEE MEETING #4



Kingwood Area Mobility Plan Steering Committee Meeting #4

GUNDA Project No. 14004-01

Date: Sept. 23, 2014, 6:00 PM

Location: Kingwood Community Center

SIGN-IN SHEET

NAME	FIRM/AGENCY	E-MAIL	TELEPHONE
BRIAN MANNING	STERLING	BMANNING & 9@ADL	2819513509
STAN SARMAN	STITEZING Committee	STAN, SARMANO ATECOM. CO.	713-20A-16A1
Mark Micheletti	11 11	Markmapa @ AOL	832-754-3350
DAVE BARROW	â _n		
Covinn Price	L C	Corina Price @insperity.co	n 28-318-3892
Charlie Dromgoole	((cdromgoole@lakehovston.	ors 281-319-8901
Caval Sutton	11	Cavulsutton 54 Ogmail	ion 195,5567
Jessica Beemer	City of Houston	jessica. beener Choustortx. gar	
Dee Price	KSA/SNC	derice 6242 Emsn.com	281-361-2040
Frances Alexander	Frebine	taleyan 509@ Adl.com	281-30-9300
Nak Den	Ossever News	usamphenonline, ch	281-378-1067
Jeffrey Weather Ford	COMIPWE	jeffrey. weether fool & houston Tx, gov	1



Kingwood Area Mobility Plan Steering Committee Meeting #4

GUNDA Project No. 14004-01

Date: Sept. 23, 2014, 6:00 PM

Location: Kingwood Community Center

SIGN-IN SHEET

NAME	FIRM/AGENCY	E-MAIL	TELEPHONE	
Maxima Colleel	FCOA	WzilAngeagnail.com	832-661-75	
Kothen Person	LSC-Knew	ed		
JEFF NIELSEN	TIRZ			

Kingwood Area Mobility Study

Lake Houston Redevelopment Authority (TIRZ #10)

Steering Committee Meeting # 4
Date: September 23, 2014




Introduction

- Introduction
- Remarks by Stan Sarman/Council
 Member Dave Martin



Recap

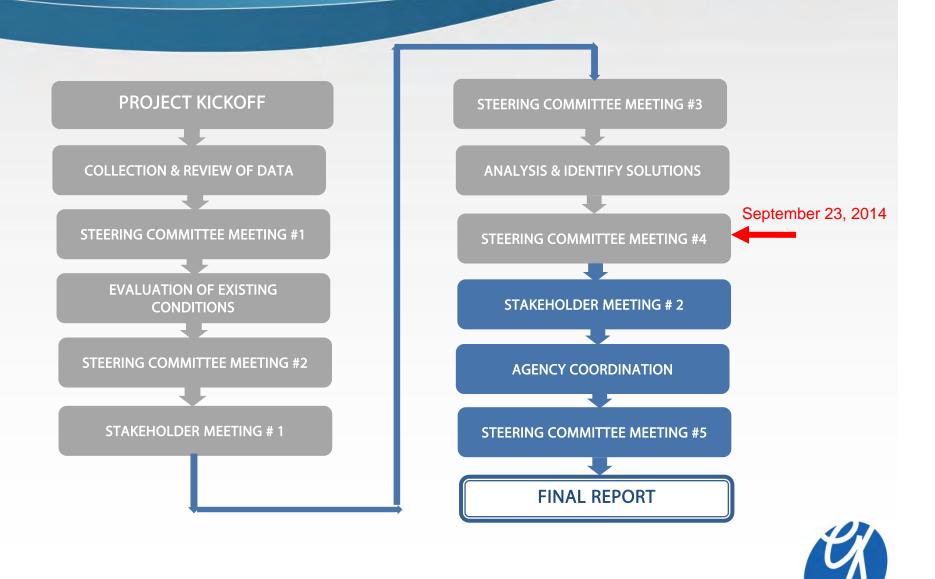

Update

- E-mails
- Survey
- Improvement Options and Analysis
- This information will be posted on the website



GOALS & MOE'S-Recap

GOALS

- Obtain community input
- Improve mobility short and long term
- Maintain same or better quality of life
- Identify funding sources
 - Educate public regarding funding sources
- Plan for future
- Safety
- Possible transit for aging population
- Pedestrian facilities as part of Street Improvements
- Public transportation
- Trolley system not typical METRO bus
- Quick fixes

MOE'S

- Less congestion
- Decrease delay/travel time
- Pedestrian safety/bicycle safety
- Vehicular safety
- Cost effectiveness
- Schedule
- Regulatory impacts
- Environmental impacts including Tree Impacts



New Developments

- Known Developments
 - Kings Creek Mixed Use 2014 Opening Year
 - Kingwood Parc Medical Office 2015 Opening Year
 - Watercrest Kingwood Senior Apartments 2015 Opening Year
 - Kings Crossings Retail 2017 Opening Year
 - Royal Brook Residential 2018 Opening Year
 - Woodridge Forest Development 2018 Opening Year
 - Riverpoint Village 2018 Opening Year
 - New Caney Middle School 2014 Opening Year
- Background Growth Rate of 2% per year up to 2020
- Approximately 4,000 trip-ends during peak hour due to these additional developments

Planned/Funded/Scheduled Roadway and Other Infrastructure Improvements

Planned Improvements & Known Development Lake Houston/Kingwood Area Mobility Study Legend



Public Input – E-mails and Survey

- 111 E-mail Comments as of September 17, 2014
 - 30 E-mail comments since our last Steering Committee Meeting # 3
 - Still receiving e-mails
- 1,075 surveys
 - Survey closed on June 30, 2014



Suggested Improvements by Citizens and Feasibility

- Reversible lanes on Kingwood Drive Not Feasible
- Woodland Hills Connection to Hamblen Analyzed
- Innovative Improvements such as roundabouts, diverging diamonds, and All-way stops Not Feasible
- Other intersection Improvements including signal timing improvements
 Analyzed
- Maintain green band for peak directions by eliminating off-peak left-turns
 Analyzed
- Direct Connector from Kingwood Drive to US 59 Analyzed
- Widen both Kingwood Drive and Northpark Drive Analyzed




Suggested Improvements by Citizens and Feasibility

- Coordinate with Union Pacific on Rail Road timings and restrict rail timings during peak hours Coordinated
- Widen Hamblen Road to 4-Lanes Analyzed
- Connection to Huffman to the east Not Feasible
- Woodland Hills Connection through FM 1960 and ultimately to BW 8
 Not Feasible




Survey Discussion

Question 1: Which Category best describes your interest?

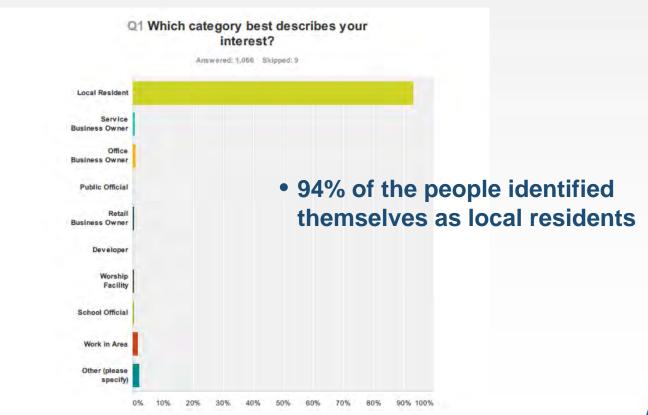





Q2: Which locations or intersections in Kingwood do you think have the most traffic issues?

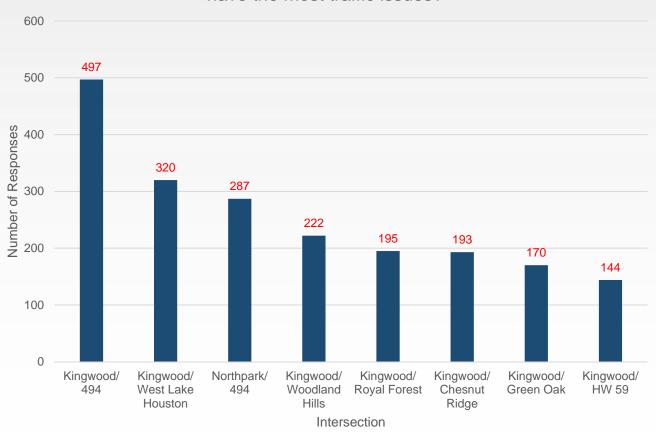




What transportation-related issues in the Kingwood area concern you the most?

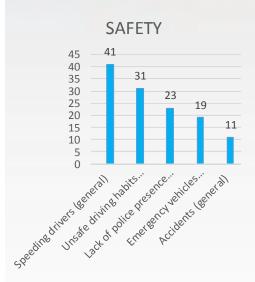


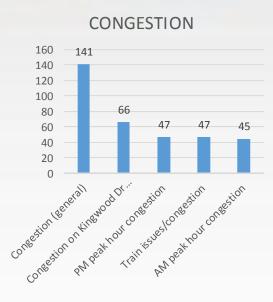




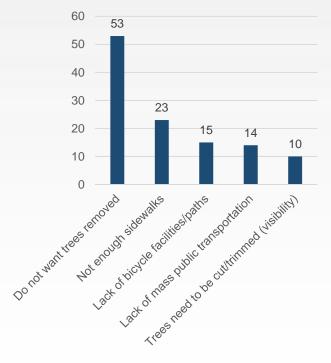



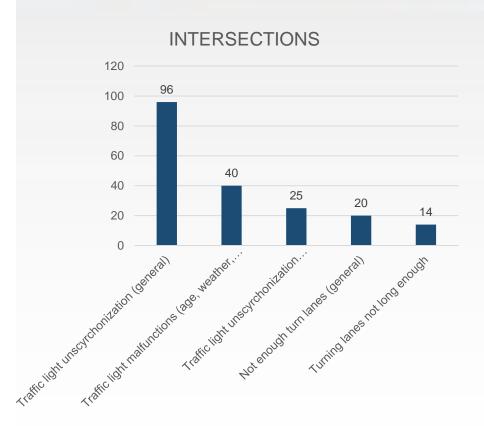


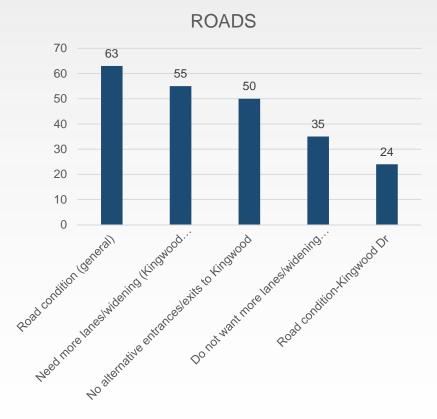





Question 4 to 9


Walking and Biking

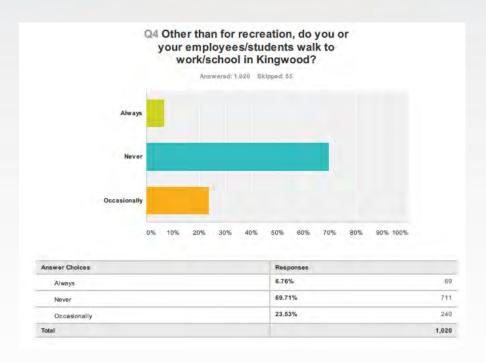

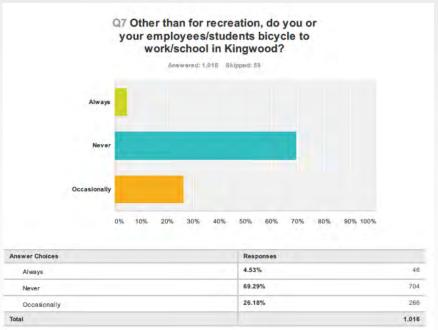





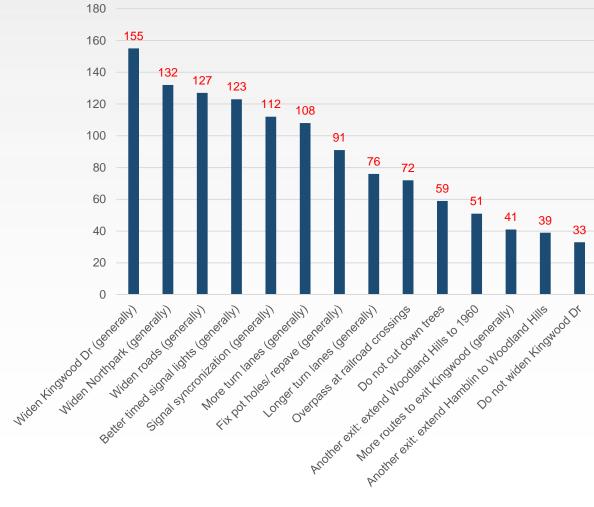




Are there any traffic-related safety concerns in Kingwood? Do you have any suggestions for these issues?





Q12 Are you willing to sacrifice trees for relief of traffic congestion? Please select one:



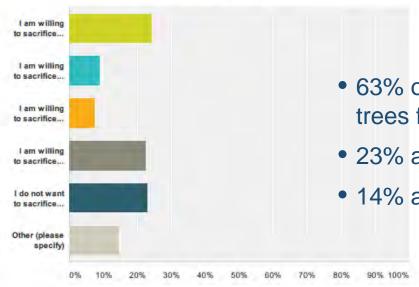


•	63%	of the people are willing to sacrifice
	trees	for savings of at least 10 minutes

- 23% are not willing to sacrifice any trees
- 14% are undecided

Answer Choices	Responses
I am willing to sacrifice trees along major thoroughfares for travel time savings.	24.12% 255
I am willing to sacrifice 25% of trees along major thoroughfares for a travel time savings of 20 minutes every day.	8.80% 93
I am willing to sacrifice 10% of trees along major thorough fares for a travel time savings of 10 minutes every day.	7.38% 78
I am willing to sacrifice some trees as long as an equal number of trees are planted elsewhere (reforestation) while achieving travel time savings of 10 minutes every day.	22.33% 236
I do not want to sacrifice a single tree, even if it means travel times continue to increase.	22.99% 243
Other (please specify)	14.38% 153
Total	1,057



Concerns by Location/Intersection

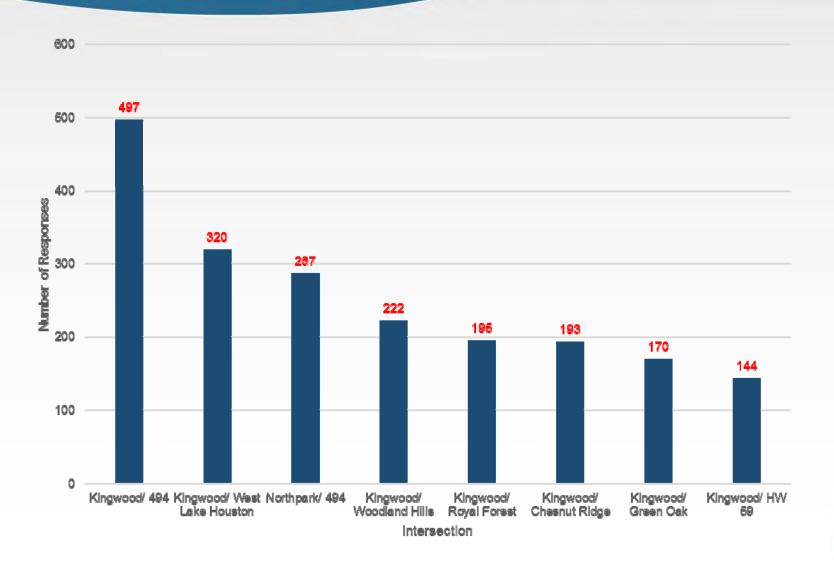



Travel Time Data

Field Collected Travel Times

AM Peak (Westbound)

On Kingwood Drive from High Valley to US 59 SB Frontage Road = 16.8 Min

PM Peak (Eastbound)

On Kingwood Drive from US 59 SB Frontage Road to High Valley = 18.4 Min

Synchro Model

AM Peak (Westbound)

On Kingwood Drive from High Valley to US 59 SB Frontage Road = 17.7 Min

PM Peak (Eastbound)

On Kingwood Drive from US 59 SB Frontage Road to High Valley = 20.3 Min



Speed Data

Kingwood High School (Westbound)						
Peak Period	Total	<25 mph	26-35 mph	36 to 45 mph	>45 mph	
6:30 AM to 7:45 AM	1,739	446	433	583	277	
2:30 PM to 3:15 PM	1,503	242	406	572	283	
School Zone Flasher Timings	6:40 AM to 7:40 AM and 2:30 PM to 3:15 PM					
Posted Speed	40 mph; School Zone Speed = 25 mph					
85th Percentile Speed	49.2 mph (DAILY BASIS)					

Kingwood High School (Eastbound)						
Peak Period	Total	<25 mph	26-35 mph	36 to 45 mph	>45 mph	
6:30 AM to 7:45 AM	973	348	532	91	2	
2:30 PM to 3:15 PM	893	379	466	47	1	
School Zone Flasher Timings	6:40 AM to 7:40 AM and 2:30 PM to 3:15 PM					
Posted Speed	45 mph; School Zone Speed = 25 mph					
85th Percentile Speed	35 mph (DAILY BASIS)					




Speed Data


Creekwood Middle School (Southbound)							
Peak Period	Total	<20 mph	20-30 mph	30 to 45 mph	>45 mph		
7:45 AM to 9:00 AM	1,157	205	726	211	15		
3:30 PM to 4:30 PM	1,233	197	522	493	21		
School Zone Flasher Timings		7:50 AM to 8:50 AM and 3:40 PM to 4:25 PM					
Posted Speed		45 mph; School Zone Speed = 20 mph					
85th Percentile Speed		44.1 mph (DAILY BASIS)					
	Cre	ekwood Middle S	chool (Northboun	d)			
Peak Period	Total	<20 mph	20-30 mph	30 to 45 mph	>45 mph		
7:45 AM to 9:00 AM	1,353	373	541	439	0		
3:30 PM to 4:30 PM	1,277	519	353	394	11		
School Zone Flasher Timings	7:50 AM to 8:50 AM and 3:40 PM to 4:25 PM						
Posted Speed	45 mph; School Zone Speed = 20 mph						
85th Percentile Speed	40.3 mph (DAILY BASIS)						



311 Calls - Signal Repair

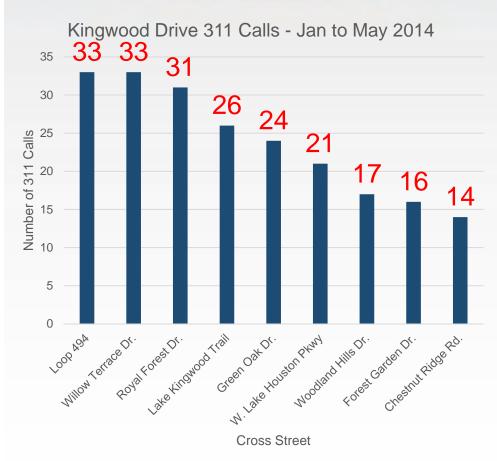

Northpark Drive 311 Calls - Jan To May 2014

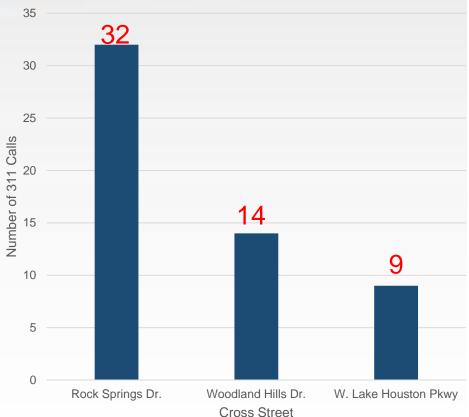



COH MTFP Thresholds

- City of Houston MTFP volume thresholds
 - *2-Lanes = 14,000 to 16,000 vehicles/day
 - ◆4-Lanes = 30,000 to 33,000 vehicles/day
 - ◆6-Lanes = 40,000 to 45,000 vehicles/day
- Kingwood Drive from US 59 to Woodland Hills Drive-Exceeded the threshold (Current Data=37K to 41K per day)
- Northpark Drive from US 59 to Woodland Hills Drive-Exceeded the threshold (Current Data=35K per day)
- West Lake Houston Parkway from Kingwood Drive to Bridge (south) – (Current Data=31K/day)

Improvement Alternatives

- 1. Intersection Improvements
- 2. Left-Turn Prohibition in Off-Peak Direction
- A. 6-Lane Kingwood Drive only
- B. 6-Lane Northpark Drive only
- C. Direct Connector from Kingwood Drive to US 59 only
- D. Direct Connector from Northpark Drive to US 59 only
- E. 6-Lane Kingwood Drive with direct connector from Kingwood Drive to US 59
- F. 6-Lane Northpark Drive with direct connector from Northpark Drive to US 59
- G. 6-Lane Kingwood Drive, 6-Lane Northpark Drive, Direct Connector from Kingwood Drive to US 59, and Direct Connector from Northpark Drive to US 59
- H. Woodland Hills Drive Extension to Hamblen Road
- I. Widening of Kingwood Drive and Northpark Drive
- J. Underpass on Kingwood Drive @ Loop 494/Rail Road
- K. Underpass on Northpark Drive @ Loop 494/Rail Road




- Traffic Signal Timing Coordination
- New Traffic Signal at Northpark Drive & Hidden Pines/Woodridge Parkway
- EBR at Northpark Drive & Hidden Pines
- EBR at Northpark Drive & West Lake Houston Parkway
- NBR at West Lake Houston Parkway & Kings Crossings Drive
- NBR at Kingwood Drive & Sorters Road
- EBR and WBR at Kingwood Drive & Loop 494
- NBR at Kingwood Drive & Royal Forest Drive
- EBR at Kingwood Drive & Green Oak Drive



- EBR at Kingwood Drive & Trailwood Village Drive
- NBR & SBR at Kingwood Drive & Chestnut Ridge Road
- EBR, WBR, EBL, WBL at Kingwood Drive & Woodland Hills Drive
- EBR at Kingwood Drive & Willow Terrace
- EBL at Hamblen Road & Forest Cove Drive
- Widening of Mills Branch Road from North of Kingwood Drive to Royal Brook Residential (New Development), north of Northpark Drive



Lake Houston/Kingwood Area Mobility Study
Intersection Improvements

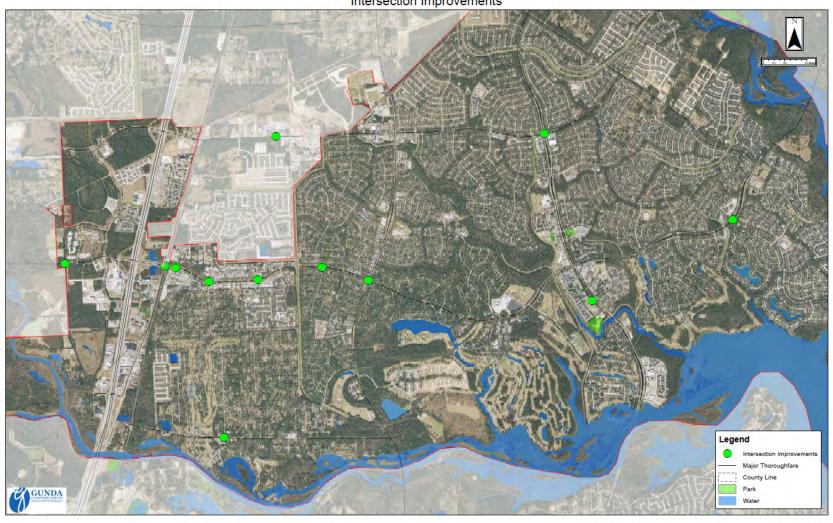



- Total Delay (in 2014):
 - Before: 1,176 Hours (AM); 1,963 Hours (PM)
 - After: 988 Hours (AM); 1,552 Hours (PM)
 - Reduction: 16% (AM); 21% (PM)
- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,302 Hours (AM); 2,131 Hours (PM)
 - Reduction: 23% (AM); 25% (PM)
- Cost of Improvements = \$16.35 Million
- Crash Reduction = 52.50%
- Tree Impacts = < 10%
- Number of Intersections at LOS E/F with Improvements (2014) = 10
- Number of Intersections at LOS E/F with Improvements (2020) = 20



Option 2: Left Turn Prohibition in Off-Peak

- On Kingwood Drive Only
- At 12 locations on Kingwood Drive, additional left-turns and acceleration lanes are required for restricted left-turns to turn around.
- Total Delay (in 2014):
 - Before: 1,176 Hours (AM); 1,963 Hours (PM)
 - After: 1,032 Hours (AM); 1,700 Hours (PM)
 - Reduction: 12% (AM); 13% (PM)
- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,560 Hours (AM); 2,596 Hours (PM)
 - Reduction: 7.5% (AM); 9% (PM)
- Cost = \$6.4 Million
- Tree Impacts = <10%
- Crash Reduction = 30%



Number of Intersections at LOS E/F with

Number of Intersections at LOS E/F with

Improvements (2014) = 10

Improvements (2020) = 20

Alternative A





Alternative A

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,081 Hours (AM); 1,845 Hours (PM)
 - Reduction: 36% (AM); 35% (PM)
- Cost of Improvements = \$31.3 Million
- Crash Reduction = 60%
- Tree Impacts = < 10%
- Number of Intersections at LOS E/F = 9
- Pros: Reduces Travel Time, Congestion, Already funded
- Cons: Some tree impacts



Alternative B





Alternative B

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,146 Hours (AM); 1,895 Hours (PM)
 - Reduction: 32% (AM); 34% (PM)
- Cost of Improvements = \$27.1 Million
- Crash Reduction = 30%
- Tree Impacts = < 10%
- Number of Intersections at LOS E/F with Improvements (2020) = 12
- Pros: Reduces Travel Time and Congestion
- Cons: Some tree impacts, multiple agency coordination, Montgomery County Roadway, Funding not readily available

Alternative C

Lake Houston/Kingwood Area Mobility Study
Alternative C: Kingwood Drive Direct Connector (Kingwood Drive to US 59 Southbound)





Alternative C

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,432 Hours (AM); 2,265 Hours (PM)
 - Reduction: 15% (AM); 21% (PM)
- Cost of the Improvement: \$50.72 Million
- Tree Impacts: <10%
- Crash Reduction = 15%
- Number of Intersections at LOS E/F with Improvements (2020) = 15
- Pros: Reduces Travel Time, Congestion, by eliminating turning movements at LP 494 and US 59
- Cons: Some tree impacts, High Cost, Aesthetics, Environmental Clearances



Alternative D

Lake Houston/Kingwood Area Mobility Study




Alternative D

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,536 Hours (AM); 2,274 Hours (PM)
 - Reduction: 9% (AM); 20% (PM)
- Cost of the Improvement: \$50.52 Million
- Tree Impacts: <10%
- Crash Reduction: 15%
- Number of Intersections at LOS E/F with Improvements (2020) = 12
- Pros: Reduces Travel Time, Congestion at Loop 494 near rail road
- Cons: Some tree impacts, High Cost, Aesthetics, Environmental Clearances



Alternative E

Lake Houston/Kingwood Area Mobility Study Alternative E: Kingwood Drive Six Lanes + Kingwood Drive Direct Connector

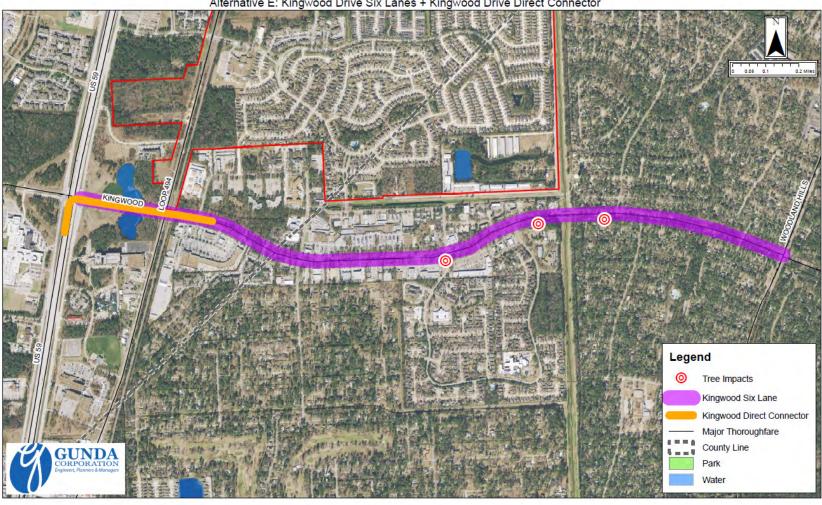



Alternative E

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,043 Hours (AM); 1,816 Hours (PM)
 - Reduction: 38% (AM); 36% (PM)
- Cost of the Improvement: \$82 Million
- Tree Impacts: <10%
- Crash Reduction: 60%
- Number of Intersections at LOS E/F with Improvements (2020) = 6
- Pros: Reduces Travel Time and Congestion, Already funded for widening
- Cons: Some tree impacts, High Cost, Aesthetics, TxDOT coordination, Environmental Clearances for over pass



Alternative F

Lake Houston/Kingwood Area Mobility Study

Alternative F: North Park Drive Six Lane + North Park Drive Direct Connector





Alternative F

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,010 Hours (AM); 1,816 Hours (PM)
 - Reduction: 40% (AM); 36% (PM)
- Cost of the Improvement: \$77.6 Million
- Tree Impacts: <10%
- Crash Reduction: 30%
- Number of Intersections at LOS E/F with Improvements (2020) = 8
- Pros: Reduces Travel Time, Congestion
- Cons: Some tree impacts, High Cost, Aesthetics, TxDOT coordination, Environmental Clearances for over pass, multiple agency coordination, Montgomery County Road



Alternative G

Lake Houston/Kingwood Area Mobility Study

Alternative G: Kingwood Drive Six Lane + Kingwood Drive Direct Connector + North Park Drive Six Lane + North Park Drive Direct Connector Legend Treelmpacts Kingwood Six Lane Kingwood Direct Connector North Park Six Lane North Park Direct Connector Major Thoroughfare County Line Water



Alternative G

Total Delay (in 2020):

Before: 1,689 Hours (AM); 2,849 Hours (PM)

After: 795 Hours (AM); 1,690 Hours (PM)

• Reduction: 53% (AM); 41% (PM)

■ Cost of the Improvement: \$159.64 Million

■ Tree Impacts: <10%


Crash Reduction: 70%

■ Number of Intersections at LOS E/F with Improvements (2020) = 0

Pros: Reduces Travel Time, Congestion, Already funded for widening

 Cons: Some tree impacts, High Cost, Aesthetics, TxDOT coordination, Environmental Clearances for over pass, Cost Prohibitive, Multiple Agency Coordination

Alternative H

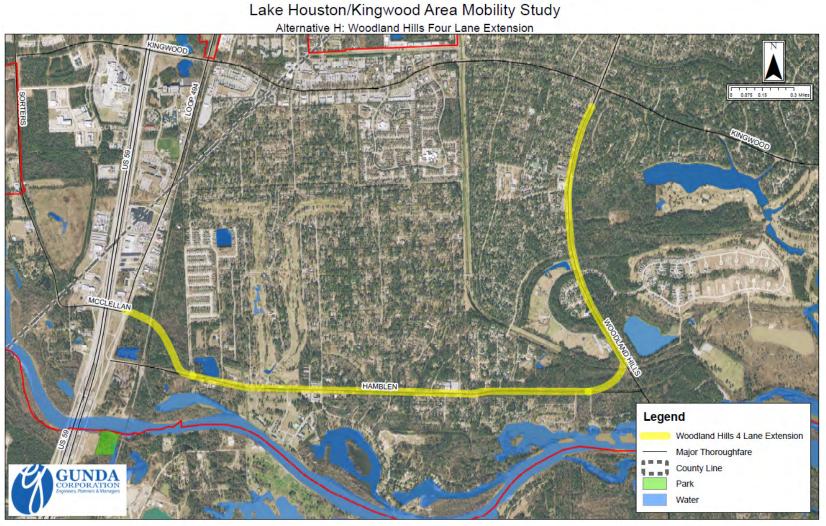



Alternative H


- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 795 Hours (AM); 1,690 Hours (PM)
 - Reduction: 53% (AM); 41% (PM)
- Cost of the Improvement: \$45.10 Million
- Tree Impacts: <30%
- Crash Reduction: 11%
- Number of Intersections at LOS E/F with Improvements (2020) = 9
- Pros: Reduces Travel Time and Congestion on Kingwood Drive,
 Provides a reliable alternative route for the area
- Cons: Significant tree impacts, not funded, ROW, environmental clearances



Alternative I

Lake Houston/Kingwood Area Mobility Study

Alternative I: Kingwood Six Lanes (US 59 to Woodland Hills) + North Park Six Lanes (US 59 to Woodland Hills)

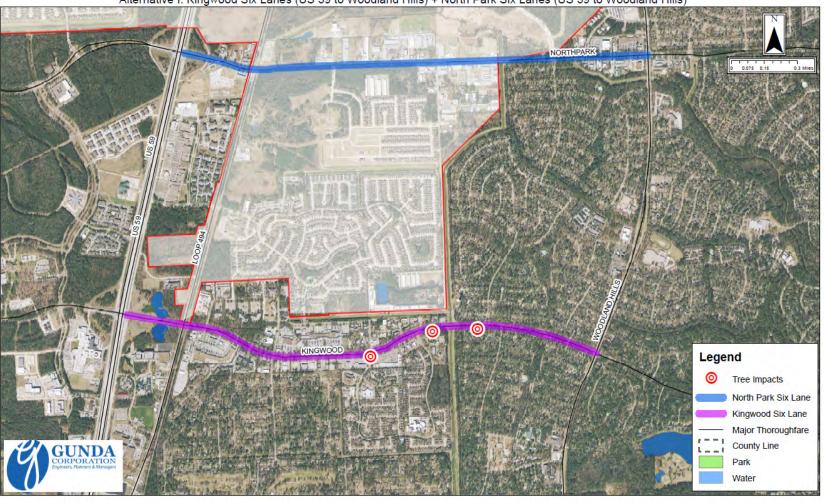




Alternative I

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 951 Hours (AM); 1,759 Hours (PM)
 - Reduction: 44% (AM); 38% (PM)
- Cost of the Improvement: \$58.4 Million
- Tree Impacts: <10%
- Crash Reduction: 70%
- Number of Intersections at LOS E/F with Improvements (2020) = 3
- Pros: Reduces Travel Time and Congestion, Partly funded
- Cons: More tree impacts, multiple agency coordination, need to identify funding for Northpark Road

Alternative J








Alternative J

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,467 Hours (AM); 2,282 Hours (PM)
 - Reduction: 13% (AM); 20% (PM)
- Cost of the Improvement: TBD
- Tree Impacts: <10%
- Crash Reduction: 7.5%
- Number of Intersections at LOS E/F with Improvements (2020) = 8
- Pros: Reduces Travel Time and congestion at Loop 494 near Railroad
- Cons: Some tree impacts, all trees between US 59 & Loop 494,
 TXDOT and UP Rail Road Coordination, Impact to Retail Driveway at Royal Forest Drive

Alternative K

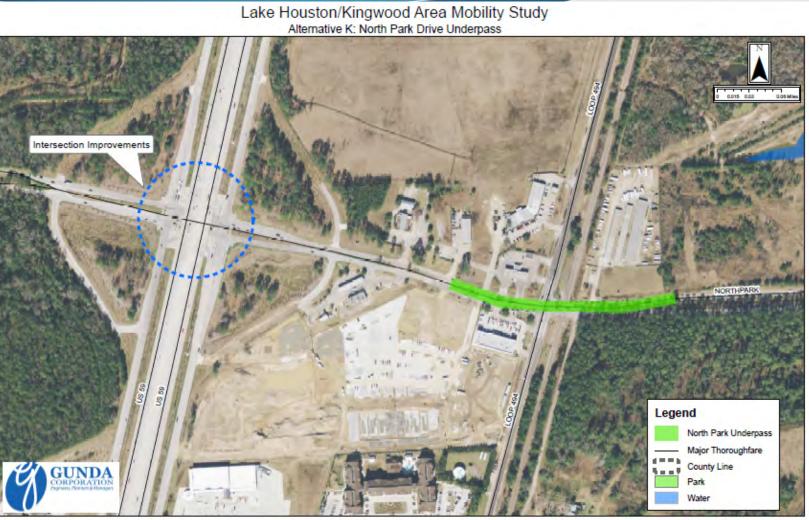



Alternative K

- Total Delay (in 2020):
 - Before: 1,689 Hours (AM); 2,849 Hours (PM)
 - After: 1,554 Hours (AM); 2,288 Hours (PM)
 - Reduction: 8% (AM); 20% (PM)
- Cost of the Improvement: TBD
- Tree Impacts: <10%
- Crash Reduction: 7.5%
- Number of Intersections at LOS E/F with Improvements (2020) = 12
- Pros: Reduces Travel Time and congestion at Loop 494 near Railroad
- Cons: Some tree impacts, all trees between US 59 & Loop 494, TXDOT and UP Rail Road Coordination.



Scoring Criteria

- Scoring MOE's
- Scoring Goals
- Weighting Factors

Improvements/Goals	Community Input	Improve Mobility (Short- Term & Long-Term)	Maintain Same or Better Quality of Life	Identify Funding Sources	Safety	Transit	Facilities	Total Score
		Plan for Future				Public Transportation		
		Quick Fixes				Trolley System		
Category Code	Α	В	С	D	Е	F	G	A to G
Weighting Factor	0	30	25	5	30	5	5	100



Hands on Exercise

- Review each improvement Option and assign score for each option
- Based on the weighting factors, the score will be calculated
- Higher the score, better the option



Next Steps

- Stakeholder Meeting #2 October 14, 2014 @ 5:30
 PM
- Open House Format with Exhibits at Stations
- Next Steering Committee Meeting Date: November 18, 2014 @ 6:00 PM
- Survey Summary and data will be posted on the website http://gundacorp.com/kingwood-mobility/



Questions?

